



SHOPIFY DAWN MIGRATION PROPOSAL

# Dawn Theme Migration, Template Consolidation and Product Experience Unification

Prepared for UNRL following a read only technical audit of the live Pipeline theme, version 7.3.0, covering the template library, the installed app stack, the tracking configuration and the product architecture.

---

PREPARED FOR

UNRL

PREPARED BY

IT-Geeks, Shopify Platinum Partner

TAGLINE

From Vision to Victory, We Power  
Your Growth

 COMPANY OVERVIEW

# About IT-Geeks

IT-Geeks is a Shopify Platinum Partner agency founded in 2015, trusted by 10,000+ clients across 10+ countries. Our 250+ specialists, including product strategists, solution architects, Shopify theme and app engineers, data and integration experts, QA analysts and growth marketers, help ambitious brands turn ecommerce ideas into scalable reality.

## End to End Shopify and Shopify Plus

- Design systems and theme development
- Headless and Online Store 2.0
- Complex migrations and replatforming
- CRO and SEO optimization
- Bespoke apps and integrations

## B2B on Shopify Plus

- Companies and price lists management
- Customer specific catalogs
- Net terms and ACH payment solutions
- Wholesale onboarding workflows
- ERP and CRM integrations

## Data Driven Delivery

- Migration playbooks and strategies
- Performance budgets and tuning
- Accessibility by design
- Analytics instrumentation
- Measurable outcomes and ROI tracking

★ INDEPENDENTLY REVIEWED

# As Voted by Our Clients

Not us, our customers say that. Their belief and trust have taken us this far in the industry.

## Shopify Experts

5.0 rating

5,000+ reviews

## Clutch

5.0 rating

300+ reviews

## Global delivery

10+ countries

10,000+ clients

### A Shopify Platinum Partner with 5,000+ five star reviews

Across independent platforms, reflecting consistent delivery quality, transparent communication and measurable outcomes over a decade of Shopify work.

### Why it matters on this project

A theme migration touches every template, every app integration, every tracking script and every URL on the store. The reviews above come from projects of exactly this shape.

Shopify Platinum Partner since 2015

10,000+ clients across 10+ countries

Dedicated data migration and QA teams

 YOUR DEDICATED TEAM

# A Team Structure Built Around This Project

One senior point of contact, with named specialists assigned to each workstream in this proposal.

## Senior Project Manager, your single point of contact

Owns scope, timeline, approvals and communication. Available during Eastern Time business hours, which covers your working day in St. Paul.

### Senior Shopify Developer

Dawn foundation, template rebuild, product architecture and custom sections.

### Senior Graphic Designer

Implementation of your Figma designs across the templates in scope.

### UX and UI Designer

Variant switcher, size selection behaviour, navigation and product discovery.

### Lead Quality Assurance Engineer

Device, browser, checkout, gating and regression testing across every gate.

### Integration Engineer

The 22 theme integrated apps, the 19 app embeds and the tracking rebuild.

### SEO Specialist

Baseline capture, redirect mapping and technical SEO verification.

Note: team structure is scalable and can be adjusted based on project requirements.


HOW WE WORK

# Our Project Management Approach

We build sites that are intuitive, accessible and responsive. Accessibility, mobile responsiveness and performance budgets are embedded from day one.

### Dedicated Team

A senior Project Manager is your single point of contact, coordinating certified Shopify developers, designers, integration engineers and QA specialists.

### Collaboration

We use Basecamp to track tasks, progress and milestones and give full visibility on timelines. If you prefer Asana, Trello, Jira or Slack we adapt.

### Availability

Your Project Manager works Eastern Time business hours. Development and QA coverage spans multiple time zones for faster turnarounds.

## Transparent workflow and communication

- Weekly progress and milestone reviews
- Video walkthroughs and feedback sessions
- Timelines and next steps documented after each checkpoint

## Quality and risk management

- Definition of done per task and per phase
- Issue and risk logs with owners and response times
- Structured change control to protect scope, budget and schedule

Basecamp as the primary channel

Weekly milestone reviews

Eastern Time working hours

 EXECUTIVE SUMMARY

## Executive Summary

UNRL runs on the Pipeline theme, version 7.3.0, roughly eighteen months behind current releases. A read only audit recorded 123 sections, 182 snippets, 18 theme blocks and 560 templates, alongside 91 installed apps, of which 22 are integrated into the theme and 19 are enabled as app embeds. Each colourway sits on its own product record, grouped by a siblings metafield pointing to a matching collection, and roughly 300 of the 560 templates are estimated to be in active use.

This proposal migrates UNRL onto Dawn as a structured rebuild rather than a straight transfer. The Figma designs are built as drawn on a clean Online Store 2.0 foundation, the template library is consolidated into flexible masters, and the product experience is unified on the front end while each colourway keeps its own product record, so Merchant Center item IDs and historical attribution data carry through untouched. The 22 theme integrated apps and 19 embeds are reworked and verified, tracking moves into Custom Pixels and app embeds, search equity is protected with a pre validated redirect map, and the store configuration is reviewed end to end. Seven workstreams, four sign off gates, a fixed fee of USD 35,000.

Signed by:  


---

**Rahul Parihar** CEO, IT-Geeks, signature and date

**Gabe Walker** Ecommerce Manager, UNRL, signature and date

 CLIENT CONTEXT AND OBJECTIVES

## Where You Are and What This Delivers

Figma designs for the homepage and product page are nearing completion, with the collection page in progress. Your in house developer is committed to other projects, which makes implementation capacity the primary bottleneck. The theme itself has been extended over years to support NFL, NHL, MLB, MNUFC, collegiate and collaboration launches, and the template library has grown with it.

**01****Build on a Shopify native foundation**

Dawn is Shopify's reference theme, so the storefront is no longer bound to a third party roadmap.

**04****Unify the product experience**

One page across colourways on the front end, with Seasonal, Core and Last Call driven by tags and metafields.

**02****Implement the designs as drawn**

The Figma work is built on a clean base rather than adapted to fit existing Pipeline sections.

**05****Rationalize apps and tracking**

The 22 theme integrated apps, the 19 embeds and the tracking stack are reworked deliberately.

**03****Consolidate the template library**

Repeating campaign patterns collapse into flexible masters, so future drops are configuration.

**06****Protect search and launch quietly**

Baseline captured first, redirects pre validated, cutover rehearsed outside peak trading.

 WHAT GOOD LOOKS LIKE

# How This Project Will Be Judged

Before scope comes the standard the finished work is measured against. These four are that standard for this engagement, and every gate is checked back against them rather than against the task list alone.

**01****Continuity above everything else**

Customers, orders, data and integrations carry through intact. Nothing about the transition should be visible to a customer.

**03****Your team runs the store without a developer**

Every section is editable in the theme editor. Building a drop page or changing a campaign is configuration, not a support ticket.

**02****A premium look and feel, held**

The designs are built as drawn, at the finish level the brand already sets, not adapted to fit a section that exists already.

**04****Historical data stays unbroken**

Product records, IDs, handles and SKUs are preserved, so Merchant Center, Triple Whale and Shopify reporting stay continuous.

These are commitments rather than aspirations. Each one is verified at Gate 3 and again after go live, and any one of them failing is treated as a launch blocker.

 AUDIT SNAPSHOT

# What the Technical Audit Recorded

Figures below come from a read only audit of the live theme and the Shopify admin. Every number is verifiable in your own store today.

|           |          |          |                |                    |                      |
|-----------|----------|----------|----------------|--------------------|----------------------|
| 560       | 123      | 182      | 91             | 19                 | 4                    |
| Templates | Sections | Snippets | Apps installed | App embeds enabled | Compiled JS variants |

## 01

### Tracking sits in three different places

GTM is present but commented out, Intelligems loads twice, and Klaviyo add to cart is hardcoded into the layout file.

## 03

### Core behaviour lives in compiled files

Four versions of the main theme script load by product template, compiled rather than editable source.

## 02

### App overlap is carrying real weight

Klaviyo Reviews shows 223 placements and Yotpo 88, two loyalty apps are enabled, and the store locator exists twice.

## 04

### Template reuse is close to nonexistent

Much of the 560 is one off campaign pages. Roughly 300 are estimated to be in active use, and this project turns that estimate into evidence.

## [↔](#) THE PLATFORM DECISION

# What Dawn Changes, Set Against Staying on Pipeline

Both routes involve rebuilding, because the Figma designs exist in neither theme today. What differs is what UNRL is standing on once the work is finished.

| DECISION FACTOR       | STAYING ON PIPELINE                        | MOVING TO DAWN                           |
|-----------------------|--------------------------------------------|------------------------------------------|
| Codebase control      | Third party, bound to their roadmap        | Shopify native, the fork is yours        |
| Theme licence         | Paid licence per store                     | Free, permanently                        |
| New Shopify features  | Arrive when the developer supports them    | Front of the queue, Dawn gets them first |
| Theme updates         | Re apply customisations, re test each time | Adopt selectively on your own schedule   |
| Product architecture  | Inherits the sibling products pattern      | Clean slate, built to your catalogue     |
| Fidelity to the Figma | Designs adapted to fit existing sections   | Built exactly as drawn, no legacy bloat  |
| Developer pool        | Specialised knowledge, slower onboarding   | Industry standard, any Shopify developer |
| Routine changes       | Dev ticket, risk to legacy customisations  | Handled in the theme editor by your team |

Both routes were evaluated against UNRL's catalogue, template library and installed app stack. This proposal scopes the Dawn route only.


SCOPE OVERVIEW

# Scope of Work at a Glance

Seven workstreams make up the migration. Each is detailed on the pages that follow, with its deliverables and its boundaries stated in full.

| # | WORKSTREAM                     | WHAT IT DELIVERS                                      | WHAT WE NEED FROM YOU                      |
|---|--------------------------------|-------------------------------------------------------|--------------------------------------------|
| 1 | Dawn foundation and design     | Dawn forked in your store, the Figma built on it      | Final Figma files, designer available      |
| 2 | Template consolidation         | Repeating patterns rebuilt as flexible masters        | Sign off on the active template list       |
| 3 | Product experience unification | One product page across colourways, records preserved | Rules for how colourways group and display |
| 4 | App integrations and embeds    | 22 integrations reworked, 19 embeds re enabled        | A decision per overlapping app             |
| 5 | Tracking and analytics rebuild | Tracking moved into Custom Pixels and embeds          | Admin access to analytics and ads          |
| 6 | SEO safe migration and launch  | Baseline, redirect map, QA either side of cutover     | Final go live approval on staging          |
| 7 | Store configuration review     | Shipping, discount, tax and settings audit            | A decision per recommendation              |

## Runs through every workstream

- Functional, accessibility, gating and checkout QA at every gate
- Documentation of each rebuilt feature, signed off before build
- Training, tutorial videos and handover into your team

## Not in scope

- New brand identity work, or redesign beyond the supplied Figma
- New API work or custom connectors, scoped separately
- Application and theme licences, and ongoing marketing work

## SECTION 02

# Scope of Work

Seven workstreams, each with its deliverables, its dependencies and its exclusions stated in full.

 WORKSTREAM 01

# Dawn Foundation and Design Implementation

Dawn is set up as a fork inside your store and your Figma designs are built onto it. Dawn's architecture differs from Pipeline's, so custom pieces are recreated rather than copied. We set that expectation here rather than in week six.

## 01

### Dawn stood up on an unpublished development theme

The live Pipeline store stays published and unaffected for the entire build. Nothing is switched until you approve the cutover.

## 03

### Custom sections rebuilt against documented behaviour

The four compiled script variants cannot be read as source, so behaviour is captured in working sessions with your developer, written down and signed off before build.

## 02

### Figma reviewed for gaps, then built as drawn

We return a written gap list covering states, breakpoints and edge cases the designs do not yet show, closed with your designer during blueprinting.

## 04

### Metafield driven product content carried across

Features, wash care, pair with, size charts, model sizing, ways to buy, pre order and badges. Definitions carry safely.

Not included in this workstream: new brand or visual identity work, and any redesign beyond the Figma your team has produced.

 WORKSTREAM 02

# TEMPLATES

## Template Consolidation

The store holds 560 templates serving campaign and drop pages across NFL, NHL, MLB, MNUFC, collegiate and collaboration launches. Your estimate is roughly 300 in active use. This workstream turns that estimate into evidence and then acts on it.

**01**

### Active template list confirmed against data

We work from your own template inventory alongside pageview data by URL, so decisions rest on traffic rather than memory.

**03**

### One offs with traffic rebuilt individually

Pages that earn their place but fit no pattern are rebuilt on their own terms rather than forced into a master.

**02**

### Repeating patterns rebuilt once as flexible masters

Where campaigns follow the same shape, one configurable template replaces many, so a drop becomes imagery and copy.

**04**

### One offs without traffic retired with redirects


Nothing is retired without your written approval, and every retired URL is mapped in the redirect sheet before the cutover.

This is the largest body of work in the project. The fee is fixed regardless of where the active count lands, so the consolidation session shapes the build order, not the invoice.

FROM 560 TO A MANAGEABLE LIBRARY

## How the Template Count Comes Down

The 560 figure is what exists, not what is used. Pageview data decides which templates earn a rebuild, which collapse into a shared master, and which retire behind a redirect.

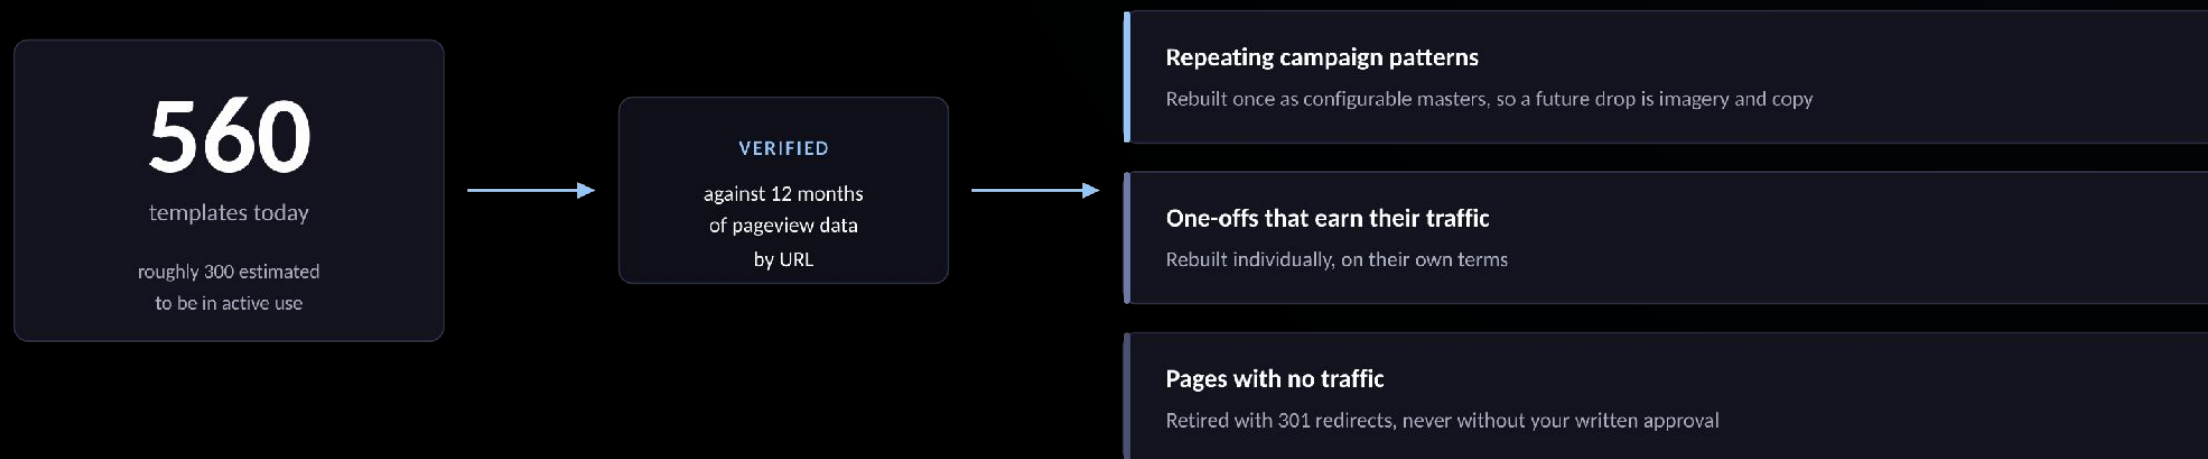

 WORKSTREAM 03

# PRODUCT

## Product Experience Unification

Each colourway is its own product today, grouped by a siblings metafield. Combined Listings was trialled and broke down where colour and inseam both vary, so this workstream unifies the experience on the front end and leaves the product records intact.

### 01

#### Requirements session before any code is written

We map how sizes, inseams, core colours and seasonal colours relate, using your rules. Nothing is assumed for you.

### 03

#### Colourways unified on the page, product records untouched

A front end variant switcher reads the siblings relationship, so one page presents every colourway without merging the products behind it.

### 02

#### Approaches presented with their trade offs

Each option is documented with its advantages, limits and maintenance cost. You choose, we build what you select, and the fixed fee holds either way.

### 04

#### Seasonal, Core and Last Call as data, not structure

Each colourway stays individually taggable, so moving a single colour to Last Call keeps working exactly as it does today.

Product IDs, handles and SKUs are preserved by design, so Merchant Center approval, Shopping history and Triple Whale attribution continue uninterrupted.

HOW THE PRODUCT PAGE WORKS

# One Page, Every Colourway, Nothing Merged


The records in your admin stay exactly as they are. The theme reads the siblings relationship and presents them as a single page, which is what keeps every product ID, SKU and tag intact.

## YOUR BACKEND, UNCHANGED

|                      |                   |
|----------------------|-------------------|
| UNRL Tee — Black     | ID 7741 · SKU BLK |
| UNRL Tee — Navy      | ID 7742 · SKU NVY |
| UNRL Tee — Sand      | ID 7743 · SKU SND |
| + 12 more colourways |                   |

Each colourway keeps its own product record, its own ID, its own SKU, its own tags.

## WHAT THE CUSTOMER SEES



One page. One URL. Every colourway.

## PRESERVED BY THIS APPROACH

- ✓ Google Merchant Center item IDs
- ✓ Triple Whale attribution history
- ✓ Last Call tagging, per colourway
- ✓ Shopify reporting continuity

### Nothing is merged in the admin.

The unification happens in the theme, on the front end only.

 WORKSTREAM 04

# App Integrations and Embeds

Of the 91 installed apps, roughly 22 are integrated into the theme, roughly 50 are back end or operational and carry over untouched, and roughly 14 are customer facing with no theme code. All 91 are assessed in a written app audit before anything moves.

## 01

### The 22 theme integrated apps reworked on Dawn

Locksmith, Klaviyo Reviews, Fit Quiz, AMP Slide Cart Drawer, Discount Genie, Zepto, Delivery Date, Instafeed, Sezzle.

## 03

### All 19 app embeds re enabled and re positioned

Embeds are stored per theme and switch off when Dawn goes live. A pre launch checklist covers every one of them.

## 02

### Locksmith rules re applied and tested with you

Locksmith spans 54 theme files. Setup is re run on Dawn, rules re applied, gated areas tested together before launch.

## 04

### Overlaps resolved, with Klaviyo and LoyaltyLion confirmed

Klaviyo and LoyaltyLion are treated as the going forward partners. Yotpo, duplicate loyalty and the other overlaps come to you.

The audit sorts all 91 apps into keep, remove, replace or now native in Shopify, each with a cost and benefit note. Theme references to PageFly, Webrex SEO, SMSBump and Sky Pilot are left behind, and nothing is uninstalled without your approval.

 WORKSTREAM 05

# TRACKING

## Tracking and Analytics Rebuild

Tracking is currently distributed across theme code, app embeds and Custom Pixels, with duplication in at least one place. Our approach is to move as much as possible out of the theme, so future theme changes stay safe.

### 01

#### Full inventory captured before anything moves

Every pixel, tag, dataLayer event and script recorded at Gate 1, so parity can be proven afterwards, not assumed.

### 03

#### Duplicate and hardcoded paths consolidated

Intelligems loads from an embed and a theme script. Klaviyo add to cart moves onto the native integration.

### 02

#### Google Tag Manager handled deliberately

The container is commented out and inactive. Triple Whale is treated as the primary source of truth, so GTM is not reinstated unasked.

### 04

#### Verified with live tools, not by inspection

Clarity, Triple Whale, Intelligems, Klaviyo and the accessibility widget confirmed firing at Gate 3.

Open item: the jelly.mdhv.io pixel remains unidentified. It is carried over, replaced or dropped on your instruction, and is not decided by us.

 WORKSTREAM 06

# SEO Safe Migration and Launch

Search visibility is the one thing a migration can quietly damage that nobody notices for weeks. Recording the benchmark before anything changes is what makes the result verifiable afterwards.

## 01

### Baseline captured before work begins

Rankings, indexed URLs, titles, meta descriptions, structured data and Core Web Vitals recorded and shared, with a minimum acceptable post launch threshold agreed in writing.

## 03

### Technical SEO verified on staging and on live

Canonicals, robots, sitemaps, structured data and internal linking checked on staging and again on live.

## 02

### Redirect map built early and pre validated

Mapping starts at Gate 2, not after launch. Every changed URL is mapped, implemented and tested before cutover.

## 04

### Rehearsed cutover with rollback available

Publish in a low traffic window, rehearsed sequence, explicit rollback points, monitoring after go live.

Because product records are preserved rather than merged, Merchant Center item IDs, product handles and historical Shopping data carry through the migration unchanged. Attribution continuity in Triple Whale is protected by the same decision.

 WORKSTREAM 07

# SETTINGS

## Store Configuration and Operations Review

A migration is the one moment when every setting in the admin is being examined anyway. This workstream turns that examination into a written set of recommendations, included at no additional cost.

**01**

### Shipping zones, rates and package dimensions

Box and package dimensions reviewed against what you actually ship, which is where stores most often overpay carrier rates.

**03**

### Tax, markets and checkout configuration

Tax settings, markets and checkout options reviewed against how the business operates today, not how it was first set up.

**02**

### Discounts, stacking rules and automatic offers

How discounts combine, where they conflict and which combinations are reachable at checkout, documented and corrected on approval.

**04**

### Recurring manual work your team does by hand

Where a repeated manual task can be replaced by a sheet or a rule, we build it and hand it over with written instructions.

Every finding is a recommendation, not a change. Nothing in your admin is altered without explicit approval, and this workstream carries no additional cost.



DELIVERY MODEL

# The Four Gate Approach

To prevent scope creep and technical surprises we work under four strict sign off gates. Nothing advances until the current gate is signed off by you.

## GATE 1

### Blueprint and Baseline

- Theme backup and offline export
- Blueprint document signed off
- Performance, CVR and SEO baseline
- Pixel and dataLayer inventory

## GATE 2

### Architecture and Layout

- Templates and sections built
- Product mapping confirmed
- Placeholder content for review
- Redirect mapping initiated

## GATE 3

### Integrations and QA

- Apps reinstalled one at a time
- Pixels verified with live tools
- Cross browser and device QA
- Gating and accessibility testing

## GATE 4

### Rehearsed Launch

- Cutover in a low traffic window
- Rollback available for 60+ days
- Monitoring at 48h, 2 weeks, 60 days
- Handover and training

Each gate ends with a written sign off from you. The live Pipeline store stays published and unaffected until Gate 4, so there is no downtime through the build.

 DELIVERY MODEL

# The Blueprint Phase and Delivery Tracking

The first one to two weeks after signature are spent turning this proposal into a specification. Nothing is built until you have signed off on precisely what will be built and when each piece arrives.

**01****A blueprint document that supersedes this proposal**

Every deliverable written down and agreed. Where the blueprint finds something this proposal missed, it governs and we honour it.

**02****A tracker covering every deliverable, with dates**

Roughly one hundred line items, each with an owner and a delivery week, so progress is a number rather than an opinion.

**03****Standing visibility while the work happens**

You hold access to the development theme and the tracker throughout, so you can see what is built and whether we are on plan.

**04****Risk decisions taken before they become expensive**

Anything that could affect data, tracking or search is raised, quantified and decided during blueprinting, not in week six.

Communication is structured around your availability. Tell us which days your team can review work and the decision points are scheduled around them rather than against them.

## QUALITY ASSURANCE

# Testing

Every workstream is tested on the development theme before it reaches your live store. You review the same checklist we use internally, and launch happens only on your written approval of the staging theme.

### Responsiveness across devices

- Seamless experience on all screen sizes
- iOS and Android mobile platforms
- Tablet devices including iPad
- Windows PC and MacBook desktops

### Performance and speed

- Measured with Google PageSpeed Insights
- Compared against the Gate 1 baseline
- Optimizations implemented as needed
- Script load reviewed after app rework

### Cross browser compatibility

- Uniform experience across web browsers
- Safari, Google Chrome and Microsoft Edge
- Legacy and current browser versions
- Rendering verified against the Figma

### Gating and access rules

- Locksmith rules tested area by area
- Athlete Portal and tier based access
- New customer accounts flows verified
- Tested with you before launch

### Order and transaction testing

- Shopping and checkout tested rigorously
- Test cards used to simulate purchasing
- Collection, product, cart and static pages
- Email templates and backend orders checked

### User experience testing

- Navigation and usability validated
- Variant switcher and size selection
- Feedback gathered and adjustments made
- Accessibility checks across templates

 DELIVERY SCHEDULE

# Phasing and Timeline Alignment

Delivery runs 30 to 45 business days from kickoff. The target is a stable, fully launched store ahead of peak trading, with exact dates fixed at kickoff and confirmed in writing.

| PHASE                       | GATE   | KEY ACTIVITY                                                   | YOUR INPUT                          |
|-----------------------------|--------|----------------------------------------------------------------|-------------------------------------|
| Kickoff and discovery       | Gate 1 | Backup, baseline capture, tracking and catalogue inventory     | Access, kickoff call, final Figma   |
| Foundation and architecture | Gate 2 | Dawn stood up, templates and sections built, product mapping   | Active template list sign off       |
| Build and integration       | Gate 3 | Designs implemented, app integrations and tracking reworked    | Decisions on apps and variant rules |
| Quality assurance           | Gate 3 | Functional, accessibility, gating, checkout and performance QA | Review of the staging theme         |
| Launch and support          | Gate 4 | Cutover, embeds re enabled, SEO verification, monitoring       | Final go live approval              |
| Peak trading freeze         | Hold   | No theme deployments once peak trading opens                   | None required                       |

Build and test off live

30 to 45 business days

Live ahead of peak trading

Zero downtime through the build. The migration happens on an unpublished development theme inside your store, so the live Pipeline site stays published and unaffected until you approve the cutover. The pre peak launch window assumes signature and kickoff within five business days of this proposal.

 THE BUILD AT A GLANCE

# Signature to Launch, Gate by Gate

Each band is work, each marker is a written sign off from you. Nothing advances until the gate before it is closed, and the live store stays published until Gate 4.

45 TO 55 BUSINESS DAYS FROM KICKOFF



\$

TIME AND COST

# Investment and Payment Schedule

This is a fixed fee engagement. The figure below does not move with hours worked, with the approach selected for the product page, or with where the active template count finally lands.

| DETAIL           | VALUE                               |
|------------------|-------------------------------------|
| Engagement       | Dawn migration, seven workstreams   |
| Timeline         | 30 to 45 business days from kickoff |
| Investment       | USD 35,000, fixed fee               |
| Support included | 30 calendar days from go live       |
| Excluded         | New API work, connectors, licences  |

## Scope boundary

This proposal covers only the functionality, features, and deliverables explicitly outlined in the document. Any additional functionality, enhancements, integrations, workflows, or requirements not expressly stated in this proposal are not included in scope and will require separate review, scoping, and commercial approval prior to implementation.

| NO. | MILESTONE   | AMOUNT       | DUE              |
|-----|-------------|--------------|------------------|
| 1   | Upfront     | \$ 7,000 USD | On signature     |
| 2   | Milestone 1 | \$ 7,000 USD | On the 30th Day  |
| 3   | Milestone 2 | \$ 7,000 USD | On the 60th Day  |
| 4   | Milestone 3 | \$ 7,000 USD | On the 90th Day  |
| 5   | Final       | \$ 7,000 USD | On the 120th Day |

Fixed fee, not time and materials. We are not paid more for slower work or additional revision rounds. If your finance team requires a different split we will accommodate it before signature.

 **COMMERCIAL NOTES**

# Applications, Themes and Third Party Costs

Application and theme licences are purchased separately by the client and their cost is not included in the proposed quote.

## Recommendations, not commitments

The applications named are recommendations. The functionalities outlined can be achieved with other applications, so they reflect capability rather than a commitment.

## Selection is confirmed with you

During execution the most suitable application is selected on the merits, with your approval. Where a replacement is recommended, you receive both licence costs side by side.

## Native first where it is possible

Where a feature can be built within Shopify without an application, we build it directly. Where an app offers more options and faster integration, we take the app route.

## Dawn carries no theme licence

Dawn is Shopify's reference theme and is free permanently, so the Pipeline licence does not carry forward. Any paid apps that remain in the stack continue on their existing terms.

Two housekeeping items noted in the audit sit outside this scope and can be handled together or separately: the polyfill.io script in the store locator section, and confirming domain restrictions on the Google Maps key.

## CLIENT RESPONSIBILITIES

# What We Need From Your Team

These are the items that can move the timeline. Each has a point in the schedule where it is needed, and if one is delayed we tell you the same week what it costs the schedule.

01

### Store, analytics and search console access

Needed at Gate 1 so the baseline, the tracking inventory and the catalogue export can begin.

04

### Product and variant rules confirmed

How sizes, inseams, core colours and seasonal colours should group, agreed in the requirements session.

02

### Active template list and retirement sign off

The single largest dependency in the project. Pageview data by URL is the most useful form.

05

### Decisions on overlapping apps

A decision per app on keep, replace or remove before anything is uninstalled or reconfigured.

03

### Final Figma files and designer availability

Designs in final form, with your designer joining the kickoff and blueprint sessions and reachable during the build.

06

### Final go live approval

Your written sign off on the staging theme before the launch window opens.

 SUPPORT AND HANDOVER

# Support and Post Launch Assistance, 30 Days

Included warranty and support period: 30 calendar days from production go live, where day zero is the public launch.

### What is included

- Bug fixes within the approved scope
- Layout and responsiveness fixes across supported devices and browsers
- Minor content updates, text edits and image swaps within existing sections
- Support for apps and integrations included in scope

### What is not included

- New features, pages or design changes
- Structural changes to navigation or site architecture
- New app installations or third party integrations
- Ongoing SEO, CRO, marketing or analytics work
- Creation of new content, designs or assets

| PRIORITY | INITIAL RESPONSE        |
|----------|-------------------------|
| Critical | Within 4 business hours |
| High     | Within 8 business hours |
| Normal   | Within 1 business day   |
| Low      | Within 2 business days  |

Channels: Basecamp as primary, a shared Slack channel if you prefer, and email for formal notices. Triage hours are Monday to Friday, 9:30 AM to 6:30 PM Eastern. Active incidents receive daily updates on business days until resolution. Rollback remains available for 60+ days after go live.



HANDOVER

# HANDOVER

## Handover and Training

The measure of success here is that your team can run the store, and launch a drop, without calling a developer. Our goal is to reduce dependency on external support for day to day updates.

### Structured training sessions

Live Zoom or Google Meet sessions walking your team through the Shopify backend: updating content, managing pages and adjusting settings such as banners, colours and fonts in the theme editor. Tailored to your team rather than generic.

### User friendly management

Dawn sections carry their own schema and settings, so your team can modify content, reorder sections and update product details from the theme editor in a few clicks rather than through a developer ticket.

### Detailed tutorial videos

Videos recorded on your own store showing how to add products, update pages, upload assets and configure device specific settings. Stored in shared Google Drive or Dropbox as a reference for current and future team members.

### Practical guidance

Training covers real scenarios such as building a collaboration page from a master template, moving a colourway to Last Call, or editing calls to action for a campaign, so changes can be made confidently.



WHY IT-GEEKS

## A Partnership, Not a Transaction

Partnering with IT-Geeks means working with a team that treats your store as an operating business rather than a deliverable. We learn how your drops run, how your catalogue is structured and how your team works before we propose changes to any of it, because a migration executed against assumptions is how stores quietly lose money.

We are candid about trade offs. Where a request carries a risk to data, tracking or search, we quantify it and put the decision in front of you rather than absorbing it silently. Where something can be built natively in Shopify instead of through another paid app, we say so, even when the app route would be faster for us.

Our working style is built around your availability rather than ours. You tell us which days you can review work, and decision points are scheduled around them. Progress is visible in a shared tracker rather than summarised in a status call, so the question of whether the project is on plan has a factual answer at any point in the engagement.

The track record is verifiable. 10,000+ clients across 10+ countries since 2015, 5,000+ five star reviews on the Shopify Experts Marketplace and 300+ reviews on Clutch. Teams across the United States, Canada, the United Kingdom and India mean coverage that spans your working day and short turnarounds on review cycles.

Shopify Platinum Partner

10,000+ clients served

250+ specialists

5,000+ five star reviews

 TERMS AND CONDITIONS

# Terms and Conditions

Please read the terms and conditions so that all the details of us working together are clear from the beginning. If you have any questions at all, please let us know, and there may be items we can sort out together.

## 01

### Timelines

Time may exceed depending upon client feedback and revisions. Timeframes exclude holidays and weekends.

## 04

### Payment schedule

The payment schedule stated in this proposal supersedes any conflicting terms in the general terms and conditions.

## 02

### Ownership of deliverables

Upon final payment, all deliverables including code, assets and documentation are work for hire and owned exclusively by the client. IT-Geeks retains no IP rights.

## 05

### Use of AI assisted tools

IT-Geeks may leverage AI assisted tools and workflows to enhance project efficiency. Client data is treated as strictly confidential and is never used to train, fine tune or share with third party AI models.

## 03

### Access and credentials

All source code, repositories, environments and credentials belong to the client. IT-Geeks works under client granted access and retains no copies after handover.

## 06

### Full terms

Full document:

<https://docs.google.com/document/d/1wb6d277-LHeG32SBUdO6hCAyFvE0bigZnqpndhBzD0/edit>

 AI USAGE AND DATA POLICY

# Our Commitment to Responsible AI

We use AI assisted tools and workflows to deliver faster turnaround and higher quality output. AI may be used during any phase of your project, and every AI assisted output is reviewed, validated and refined by our team before it becomes a deliverable. No client facing work is shipped without human oversight and approval.

## How we protect your data

All client data, including store data, customer records, business logic, credentials and proprietary content, is treated as strictly confidential

Client data is never used to train, fine tune or improve any third party or internal AI model

Where AI tools are employed we use enterprise grade platforms with data processing agreements that prohibit model training on customer inputs

Access to client data within AI workflows is limited to authorized project team members, under the same confidentiality obligations as our terms

Upon project completion and handover, no client data is retained in AI tool environments

Your rights: if you prefer that AI assisted tools are not used on any part of your project, tell your Project Manager and we will accommodate it, though this may result in extended delivery timelines. You may request details on which tools were used at any point during the engagement.

# Thank You
